



KAYAN

Connecting Excellence. Empowering Growth.

06 a MANAGED DELIVERY

Managed Delivery Operating Standard

معيّار تشغيل التنفيذ المُدار

WHAT THIS IS

How Kayan turns client demand into governed, escrow-protected delivery by verified talent.

A Yemeni operating institution ♦ Aden
Kayan Innovation, Entrepreneurship & Work Environments LLC

OWNER: CEO (MAHER FAISAL SAEED FAREA) ♦ CONFIDENTIAL — INTERNAL

Effective 30 June 2026

What this is	The operating standard for Kayan's primary revenue engine — every managed project, from first lead to close-out.
Owner	CEO, holding the Delivery Lead role on an interim basis until a Delivery Lead is appointed.
Why it exists	To guarantee delivery and protect client money through one governed process — the institution's competitive moat.
How it is used	Every project passes the ten gates G0–G9 in order; no gate is skipped; no productive work begins before escrow is funded.
Who it binds	CEO, Delivery Lead, Pod Leads, QA reviewers, Finance & Admin Lead, and all engaged talent.
Forms & tools	Platform gates, Project Tracker (KAY-OPS-DEL-002), CRM, escrow sub-account, QA checklists (KAY-OPS-MD-005), MSA (KAY-CON-001), SOW (KAY-CON-002), Talent Registry / Kayan Card.
Key risks	Work begun unfunded; a skipped gate; quality failure reaching a client; escrow misposted as revenue; under-verified talent.
Review	Annually, or whenever the gate model or the QA framework changes.

01 ENGINE

What Managed Delivery Is

Clients don't just get freelancers — they get a governed process, with accountability at every stage.

Managed Delivery is Kayan's primary revenue engine. It converts client demand into governed, escrow-protected delivery by verified talent pods, and earns Kayan a net fee of 20% of gross project value (15% for light engagements, within a 15–22% band). Kayan acts as a managing agent: it engages and manages the talent, guarantees delivery to the client, and holds the client's money in trust until work is accepted. The promise to the market is simple — execution, verified. This standard is how that promise is kept on every project, whether a USD 200 micro engagement or a USD 15,000 enterprise build.

02 LAW

The Five Founding Rules

- ♦ **No SOW + No Escrow (100% funded) = No Work.** No productive work begins before Gate G3 escrow funding is confirmed.
- ♦ **No gate is skipped.** Gates may be accelerated (a Rush carries +10%) but never bypassed.
- ♦ **Three-layer QA is mandatory** for every deliverable before a client sees it.

- ♦ **Dual approval on every financial transaction** — payments and escrow releases require the CEO and the Finance & Admin Lead.
- ♦ **A pod deploys only** when its Pod Assurance Score is at least 70.

03 PROCESS

The Gate System — G0 to G9

Ten gates. No gate passes without documented evidence.



FIGURE ♦ *The ten gates — escrow is the trust gate at G3; acceptance, net-fee recognition and close at G9.*

Gate	Name	What happens	Owner	Exit evidence
G0	Lead Qualification	Screen inbound leads for fit, viability, and ability to pay; log in the CRM.	CEO / BD	CRM entry; qualify or decline with reason
G1	Feasibility & Discovery	Assess delivery with quality, on time, at or above the 15% margin floor; confirm verified talent and scope.	CEO + Delivery Lead	Feasibility note; margin $\geq$ 15%
G2	Design, Proposal & SOW	Design the solution, form the pod concept, price the work, draft and sign the SOW (deliverables, acceptance criteria, milestones, value, net fee).	CEO + Delivery Lead	Signed SOW
G3	Contract & Escrow Funded	Execute MSA/SOW; client funds 100% of value into the Aden Bank escrow sub-account; issue the project ID. No work before this.	CEO + Finance	Bank confirmation + Finance log
G4	Pod Assembly & Kick-Off	Assemble a verified pod (Tier 2+); assign the Pod Lead; brief the team; onboard the client; begin Milestone 1.	Delivery Lead	Pod roster + skills matrix + kick-off
G5	Execution & Checkpoint	Work in progress; direction checked at 25-30%; weekly check-ins; blockers escalated within 24 hours.	Pod Lead	Progress log + drafts

Gate	Name	What happens	Owner	Exit evidence
G6	Mid-Build & Variance	Comprehensive quality check at 50-60%; financial variance reviewed against budget.	Delivery Lead + QA	Mid-build review + variance check
G7	Pre-Delivery QA	Full three-layer QA against the SOW acceptance criteria; defects remediated before submission.	QA Lead + Delivery Lead	Signed QA checklist; QA score ≥ 4.0
G8	Client Submission & Review	Deliverable submitted; the client has 5 business days to accept or return it with specific reasons; silence is deemed acceptance per the MSA.	Delivery Lead + CEO	Client sign-off or 5-day expiry
G9	Acceptance, Release & Close	On acceptance, dual authorisation releases the talent share (80%); the net fee is recognised (GL 4300); the 2% holdback (GL 2175) is retained 30 days then released; the project is archived, lessons captured, client survey and talent feedback recorded.	CEO + Finance + Delivery Lead	Payment & payout log; close report; holdback release

04 MONEY

The Trust Gate & Money Flow

Escrow is held in trust — it is never Kayan's money until the work is accepted.

At Gate G3 the client funds 100% of the project value into the dedicated Aden Bank escrow sub-account, booked as a liability (GL 2170). The escrow ledger is reconciled to the sub-account daily and must match to the dirham. As milestones are accepted the talent share is released; at Gate G9 the net fee is recognised to revenue (GL 4300) and the 2% quality holdback (GL 2175) is retained for 30 days, then released. No project is priced below the 15% margin floor; any deviation requires the CEO's approval.



Escrow is never revenue. Only the net fee is recognised — at client acceptance (G9).

FIGURE ♦ Client money through the gates — liability until accepted, fee recognised at G9.

05 TALENT

Verification & the Trust Ladder

Verification protects the client and rewards the talent — and it is recorded on the Kayan Card.

Talent is engaged through a progressive verification ladder. Each tier unlocks more pod access and a higher rate, and is reflected in the holder's Kayan Card — the lifetime credential that records identity, verification level, and work history. Only Tier 2 and above join paid pod roles, and a pod deploys only when its Pod Assurance Score reaches 70.

Each tier unlocks more pod access and a higher rate — and a higher Kayan Card level.

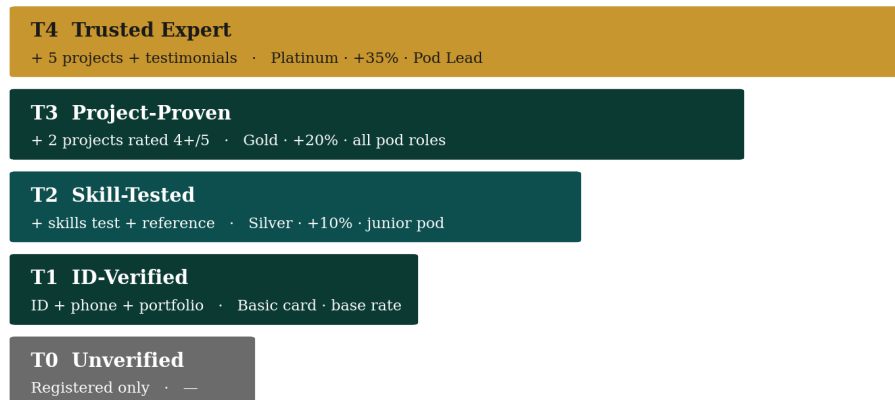


FIGURE ♦ The trust ladder — from registration to Pod-Lead-eligible Trusted Expert.

06 QUALITY

Quality Assurance

Quality is not a department. It is the company.

Three laws govern quality: nothing reaches a client without passing a documented QA gate; if it was not checked, it was not delivered; and every review is scored and feeds back into the talent record. Every deliverable passes three layers of review before submission.

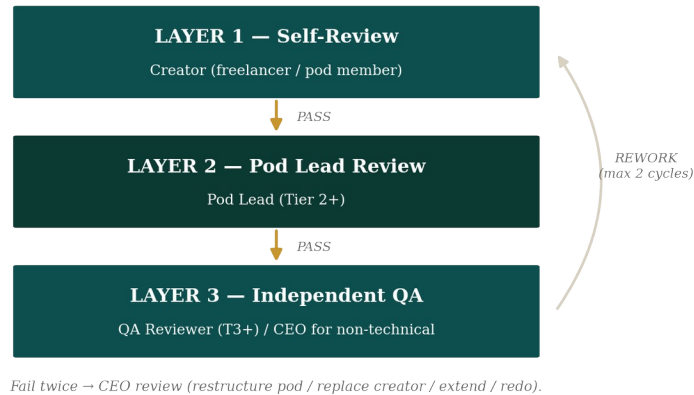


FIGURE ♦ The three-layer QA model — self-review, pod-lead review, independent QA.

Each deliverable is then scored against five weighted dimensions to produce a QA Score out of 5.0.

Dimension	Weight	Threshold to pass
Completeness	25%	100% of SOW items present, correct format and quantity
Quality	30%	Zero critical defects; meets acceptance criteria; professional standard
Functionality	20%	Works as specified across the intended platform/devices
Usability & presentation	15%	Clear, well-formatted, client-ready
Compliance & acceptance	10%	Matches SOW acceptance criteria and Kayan brand

Scoring: each dimension is scored 1–5 and weighted. A weighted score of 4 or more passes; 3 is a conditional pass with final polish; 2 returns for rework with specific feedback; 1 fails and escalates to the CEO. A deliverable that fails QA twice (two rework cycles) triggers a CEO review — restructure the pod, replace the creator, extend with client communication, or absorb a complete redo. The same discipline applies to a USD 200 micro project and a USD 15,000 enterprise engagement; only the depth and number of reviewers differ.

07 PEOPLE

Roles & Responsibilities

Role	Responsibilities	KPIs
Delivery Lead (interim: CEO)	Owens the pipeline end to end — feasibility, design, pod assembly, mid-build, submission, close.	On-time delivery; acceptance rate; throughput (days to delivery)
Pod Lead (Tier 4)	Runs the pod; Layer-2 QA; milestone delivery; escalates blockers within 24h.	First-try QA pass; rework rate; on-time milestones
QA Reviewer (Tier 3+ / CEO)	Independent Layer-3 QA against the five-dimension framework.	QA score; escaped defects (zero)
Finance & Admin Lead	Escrow administration; dual-sign; net-fee recognition; holdback release; daily reconciliation.	Escrow match 100%; holdback auto-release >95%
CEO	Approvals, escalations, floor-price exceptions, client relationships.	Margin floor held; escalations resolved
Talent	Deliver to standard; Layer-1 self-review before submission.	Client rating $\geq$ 4/5; zero disputes

08 EXCEPTIONS

Exceptions, Change & Disputes

No gate is ever skipped; a Rush accelerates the timeline for a 10% premium but bypasses nothing. Any change to scope, value, or dates is made only through a signed Change Request; work outside an approved Change Request is not performed and not paid. Each accepted handover is recorded on a Delivery Note. Disputes and any refund follow the Refund & Cancellation Policy, and the 15% margin floor is never crossed without the CEO's approval.

09 PERFORMANCE

KPIs & Tools

Metric	Target	Why it matters
On-time delivery	> 90%	Client satisfaction; churn and refund risk
Escrow compliance	100%	Legal compliance; bad-debt and fiduciary risk
QA gate pass (first try)	> 85%	Quality; rework eats margin
Talent utilisation (Tier 2+)	> 70%	Pod readiness; assembly delays
Average days to delivery	< 21 (standard)	Throughput; cash conversion

Metric	Target	Why it matters
Holdback auto-release	> 95%	Cash-flow efficiency; talent satisfaction

The standard runs on the platform gates, the Project Tracker (KAY-OPS-DEL-002), the CRM, the escrow ledger, the QA checklists (KAY-OPS-MD-005), the MSA and SOW, and the Talent Registry / Kayan Card.

Connected Systems & Instruments

Master Service Agreement (KAY-CON-001) ♦ Scope of Work (KAY-CON-002) ♦ Financial Policy (KAY-FIN-POL-001) ♦ Finance & Admin SOP (KAY-FIN-SOP-001) ♦ Governance Charter (KAY-GOV-002) ♦ Accountability & Decision Rights (KAY-GOV-ACC-001) ♦ Anti-Fraud & COI Policy (KAY-GOV-006) ♦ QA Framework & Gate Checklists (KAY-OPS-MD-005) ♦ Project Tracker (KAY-OPS-DEL-002) ♦ Talent Engagement Terms ♦ Change Request ♦ Delivery Note ♦ Refund & Cancellation Policy ♦ Kayan Card / Talent Registry ♦ Accounting Engine.

